SELECTURE AFRICA

DIGITAL PLATFORM STRATEGY / 2026

THE WEBSITE DEVELOPMENT ROADMAP

A five-step implementation plan for an Africa-focused recruitment, membership and talent-development platform.

NEXT.JS / TYPESCRIPT / SCSS / SUPABASE / CLOUDINARY

CORPORATE-FIRST. WEBSITE-FIRST. BUILT TO SCALE.

01 / PROJECT VISION

Build the website first. Design for the larger ecosystem.

Selecture Africa is being repositioned from a traditional executive-search and personnel-outsourcing firm into a digitally enabled African talent solutions platform. The website is the first release; a mobile application is intended for a separately funded later stage.

Primary users: Corporate organizations and employers. Secondary users: African professionals, diaspora talent and training participants.

Success criteria

- Communicate the company's established recruitment and outsourcing capabilities with international credibility.
- Allow organizations to register, request services and monitor submissions.
- Allow individuals to register, create professional profiles and express interest in programs.
- Support the proposed four-course training initiative through course information and registration.
- Give Selecture staff a secure back office to manage requests, accounts, programs and content.

Recommended product positioning

An Africa-focused talent solutions platform connecting organizations with skilled professionals while creating pathways for training, workforce development, recruitment, outsourcing and international opportunities.

Confirmed direction vs proposed implementation

SOURCE-ALIGNED REQUIREMENTS	PROPOSED IMPLEMENTATION
Two membership types; client membership primary	Separate corporate and individual registration, profiles and dashboards
Recruitment and personnel outsourcing services	Corporate service request forms with staff-managed request statuses
Program information and training signups	Programs catalog, detail pages and registration records
Newsletter, personalized updates, feedback	Email preference records, notifications and feedback forms
Website first; application later	Modular backend and responsive website prepared for reuse

02 / BRAND & TECHNOLOGY

A modern corporate foundation

Proposed visual identity

Refine the brochure's maroon heritage into a premium international visual language. These are exploratory design choices, not yet client-approved.



Midnight Navy #19263D
Burgundy #782F47
Champagne Gold #B79660
Warm Ivory #F7F5F0
Forest Green #243B35

Typography: Plus Jakarta Sans for user interfaces and navigation, paired with DM Serif Display for selected large editorial headlines. Styling: understated motion, generous spacing, high-contrast type, original photography, rounded functional UI elements, mobile-first grids. Avoid neon, 3D and excessive gradients.

Selected technical stack

LAYER	TECHNOLOGY / RESPONSIBILITY
Frontend	Next.js App Router + TypeScript; server rendering, routing and SEO
Styling	SCSS Modules, shared variables, accessible responsive components
Backend	Next.js Server Actions + Route Handlers with server-side validation
Database	Supabase PostgreSQL, migrations, constraints and RLS
Authentication	Supabase Auth for corporate, professional and admin accounts
Images / videos	Cloudinary for approved public media, transformations and optimized delivery
Sensitive documents	Private Supabase Storage for CVs and verification materials
Transactional email	Resend or equivalent; verified sending domain and unsubscribe workflow
Hosting / DNS	Vercel production deployment; Cloudflare-controlled domain and DNS
Product analytics	PostHog or equivalent, subject to privacy settings

Architecture rule

All protected actions must be authorized on the server. Database RLS should enforce data ownership; Cloudinary must not become public storage for private CVs or identity documents. All media uploads need type, size and permissions checks.

03 / STEP ONE

01 — Discovery, architecture & database

Target: Days 1–3

Establish an approved first-release specification before development. Initialize Next.js, TypeScript, SCSS Modules, Supabase, environment configuration and version control.

Key work packages

- Confirm exact pages, roles, membership rules, service request types, training content and acceptance criteria.
- Define corporate, individual, admin and super-admin permissions and the relationship between organization members.
- Initialize App Router route groups, reusable components, environments and source-control workflows.
- Model PostgreSQL relationships, schema migrations, uniqueness constraints and Row Level Security.
- Establish content ownership, privacy requirements, retention periods and media upload restrictions.

Initial relational database tables

TABLE	PURPOSE
profiles	Common authenticated-user data and account type
organizations / organization_members	Organization profiles and authorized staff members
professional_profiles	Skills, experience, location, career details and visibility controls
service_requests / submissions	Recruitment inquiries, outsourcing requests and follow-up statuses
programs / program_registrations	Course metadata, cohorts and participant registration
notification_preferences	Newsletter opt-ins, message preferences and consent history
media_assets	Cloudinary public identifiers and upload metadata
audit_logs	Sensitive admin actions, ownership changes and compliance events

Acceptance checkpoint

Approved sitemap, role-permission matrix, wireframes, versioned database migrations, reproducible local setup and working authentication scaffolding.

04 / STEP TWO

02 — Design & build public pages

Target: Days 4–8

Build the full responsive, corporate-facing public website. The homepage should prioritize Hire Talent and offer Join as a Professional as the clear secondary route.

Recommended sitemap

PAGE	CORE SECTIONS / PURPOSE
Home	Hero, employer CTA, talent CTA, company value, featured services, sectors and programs
About	Company background, mission, vision, leadership, global reach and values
Our Services	Executive search, outsourcing, volume resourcing, team building, background checks, document verification
Industries	Banking/finance, FMCG, technology, oil/gas, consulting, legal, public sector
For Employers	Recruitment benefits, corporate membership and request-talent journey
For Professionals	Individual memberships, employability, careers and program opportunities
Programs & Training	Program catalog, details, instructors where confirmed, participant registration
Insights & Resources	Articles, guidance, company news and thought leadership
Contact & Feedback	Lagos/London information, service inquiries and feedback
Authentication	Register, sign in, forgot/reset password, confirmation states

Design deliverables

- Brand foundations: typography, color tokens, spacing, iconography, buttons, form fields, card and navigation patterns.
- Responsive templates for desktop, tablet and mobile, including clear empty, error and loading states.
- Trust-led content that preserves existing Selecture recruitment services rather than presenting an unsupported job marketplace.
- SEO-ready public page metadata, semantic headings and accessible interactive components.

Acceptance checkpoint

Approved visual system and production-quality public pages at desktop and mobile sizes, populated with validated corporate copy and photography.

05 / STEP THREE

03 — Memberships & business functionality

Target: Days 9–14

Convert the website into an operational recruitment and talent platform with secure registration, user journeys and administration.

Corporate membership — primary commercial journey

- Register and verify a corporate contact; create and edit an organization profile.
- Submit executive search, workforce outsourcing, screening or training service requests.
- View requests and staff-updated statuses; receive confirmation and follow-up messages.
- Manage communication preferences and organization contacts subject to account permissions.

Individual membership — secondary journey

- Create a professional account, profile, professional interests and skills information.
- Upload CVs to private storage and control exposure of candidate information.
- Discover listed training programs, register and check submission history.

Administration

- Manage members, company profiles, program listings, applications, service requests and public website content.
- Review, assign and update requests; manage newsletter segments and basic reporting.
- Record important administrative changes and apply least-privilege account permissions.

Illustrative first-release service workflow



The full six-stage executive search and outsourcing processes in the original brochure remain staff-led unless a later applicant-tracking module is approved.

Acceptance checkpoint

End-to-end tested corporate and individual signups, service request status changes, program registration, private uploads and working admin functions.

06 / STEP FOUR

04 — Media, messaging, security & QA

Target: Days 15–18

Integrate production services and verify the website before real members and corporate clients use it.

Cloudinary media implementation

- Store company photos, promotional video, team imagery and program banners in Cloudinary; use automatic transformations and compression.
- Use signed uploads or restricted presets, validated MIME types, size limits and safe asset lifecycle rules.
- Retain Cloudinary IDs and metadata in PostgreSQL. Keep CVs and sensitive material in private object storage.

Communication implementation

- Send transactional welcome, verification and request-confirmation emails.
- Notify staff of high-priority corporate requests and registrations.
- Store newsletter preferences; support opt-out, personalization and feedback submission.

Security & quality gates

AREA	REQUIRED CHECK
Authentication / RLS	Users cannot read or change another account's private records
Authorization	Protected actions recheck permissions server-side
Input safety	Zod validation, escaping, rate limits and anti-spam protection
Sensitive data	Private CV access, consent, retention and secure file delivery
Accessibility	Keyboard flows, labeling, focus states, contrast and reduced motion
Responsiveness	Representative iOS/Android phone, tablet and desktop breakpoints
Functionality	Signups, uploads, submissions, notifications, staff actions and errors
Operations	Logging, monitoring, backup/restore testing and rollback readiness

Acceptance checkpoint

Written QA checklist completed, identified critical defects resolved, production email delivery tested and security permissions reviewed.

07 / STEP FIVE

05 — Launch, handover & growth readiness


Target: Days 19–21

Launch at selecture.org, reportedly already purchased and managed in Cloudflare; verify ownership and DNS access before deployment.

Production rollout checklist

- Deploy the production Next.js application to Vercel and apply reviewed Supabase database migrations.
- Connect domain and SSL through Cloudflare; check DNS and redirects, headers and secret handling.
- Configure sender-domain authentication, transaction emails, sitemap, SEO metadata and Open Graph images.
- Test realistic user journeys from landing page to confirmation and admin follow-up.
- Complete client signoff, rollback procedures, monitoring and administrative training.
- Hand over source repository, environment inventory, domain/deployment documentation and maintenance ownership.

Indicative implementation timeline

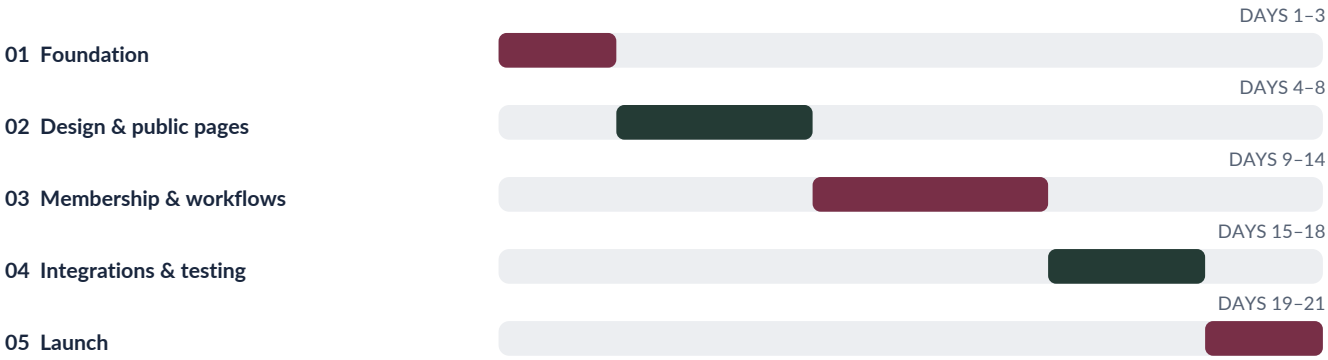

Scheduling assumption

The 21-day target is aggressive and assumes an experienced developer, rapid client approvals, ready text/assets and limited revisions. Timelines should be reset if full applicant tracking, paid memberships or an LMS are added.

Phase-two opportunities, not included in initial scope

- Full applicant tracking, matching, employer candidate review and interview coordination.
- Online learning delivery, assessments, certificates, paid programs and progress tracking.
- Subscriptions, billing, payroll management, enterprise integrations and an independently funded mobile app.

08 / DELIVERY REFERENCE

Repository architecture & release boundaries

Suggested source code organization

```
selecture-africa/
  src/app/
    (public)/        company, services, sectors, programs
    (auth)/          sign-in, registration, password reset
    (dashboard)/     corporate, individual
    (admin)/         operational back office
    api/             webhooks, signed upload endpoints
  src/components/    ui, forms, navigation, layouts
  src/features/      memberships, recruitment, programs
  src/lib/           supabase, cloudinary, validators, auth
  src/styles/        globals.scss, _variables.scss, mixins
  src/types/         shared application types
  supabase/migrations/
  public/
```

Version-one delivery boundary

INCLUDED IN WEBSITE MVP	LATER / SUBJECT TO APPROVAL
Public website and complete service presentation	Native iOS and Android apps
Individual and corporate membership registration	Membership payment tiers and subscription billing
Professional profiles and private CV uploads	Automatic candidate-to-job matching
Recruitment/outsourcing service submissions	Full applicant tracking and employer job-board workflows
Training catalog and program registration	LMS, lessons, exams, certificates and video streaming
Basic admin and content management	Advanced payroll, workforce management and partner integrations
Emails, privacy controls, reporting essentials	Advanced predictive analytics and AI assessment

Client decisions still required

- Confirm legal entity, domain and infrastructure access, approved brand assets and final company copy.
- Define free/paid membership rules, program registration terms and employer permissions.
- Confirm the four training course titles, trainers, delivery dates and whether training content is in the website.
- Sign off exact first-release features, budget, milestones, success criteria and after-launch support.

Reference basis

Prepared from the Selecture Africa consolidated project brief (13 October 2026), the original six-page Selecture Africa brochure and the proposed five-step website roadmap. The technology stack, timeline, palette, database design and implementation details are planning recommendations rather than an approved contract.

Go-live acceptance summary

The website is release-ready when both audience journeys work from discovery to submission, administrative review is operational, all production communications arrive correctly, and private member information cannot be accessed across accounts.

Client handover package

- Production URL and verified Cloudflare/Vercel ownership and access.
- Secure transfer of infrastructure credentials, environment keys and administrator permissions.
- Versioned project code, Supabase migrations, technical documentation and deployment runbook.
- Content editing guidance, support responsibilities, maintenance plan and issue escalation contacts.

Roadmap guidance

This roadmap is a comprehensive implementation proposal rather than a signed technical specification. Course titles, commercial membership rules, deadlines, partner roles and investment claims require direct stakeholder approval before being treated as contractual requirements.

SELECTURE AFRICA / Corporate recruitment. African talent development. A scalable digital future.
